


ID	Stage	SDLC Phase	Deliverable	Task Name	Schedule Status	Duration	Start	Finish
0				<b>Project Work Plan (Schedule) Complex v1</b>		<b>224.5 days</b>	<b>Thu 10/29/09</b>	<b>Tue 10/26/10</b>
1			<b>Stage</b>	<b>Schedule Template</b>		<b>224.5 days</b>	<b>Thu 10/29/09</b>	<b>Tue 10/26/10</b>
2				<i>Project Starts</i>		<i>0 days</i>	<i>Thu 10/29/09</i>	<i>Thu 10/29/09</i>
3	<b>Concept</b>	<b>N/A</b>	<b>Stage</b>	<b>Concept Stage</b>		<b>18 days</b>	<b>Thu 10/29/09</b>	<b>Tue 12/1/09</b>
4	Concept	N/A	ADM	Develop Concept Statement		5 days	Thu 10/29/09	Wed 11/4/09
5	Concept	N/A	ADM	Determine Size Estimating (ROM)		5 days	Thu 11/5/09	Mon 11/16/09
6	<b>Concept</b>	<b>N/A</b>	<b>ADM</b>	<b>Concept Stage Approval</b>		<b>8 days</b>	<b>Tue 11/17/09</b>	<b>Tue 12/1/09</b>
12	<i>Concept</i>	<i>N/A</i>	<i>ADM</i>	<i>Concept Stage Approved</i>		<i>0 days</i>	<i>Tue 12/1/09</i>	<i>Tue 12/1/09</i>
13	<b>Initiating</b>	<b>N/A</b>	<b>Stage</b>	<b>Initiating Stage</b>		<b>3 days</b>	<b>Wed 12/2/09</b>	<b>Mon 12/7/09</b>
14	<b>Initiating</b>	<b>N/A</b>	<b>Proj Charter</b>	<b>Project Charter</b>		<b>2 days</b>	<b>Wed 12/2/09</b>	<b>Thu 12/3/09</b>
15	Initiating	N/A	Proj Charter	Complete General Information		1 day	Wed 12/2/09	Wed 12/2/09
16	Initiating	N/A	Proj Charter	Obtain Project Charter Approval		1 day	Thu 12/3/09	Thu 12/3/09
17	<i>Initiating</i>	<i>N/A</i>	<i>Proj Charter</i>	<i>Project Charter Approved</i>		<i>0 days</i>	<i>Thu 12/3/09</i>	<i>Thu 12/3/09</i>
18	<b>Initiating</b>	<b>N/A</b>	<b>ADM</b>	<b>Issue Log</b>		<b>1 day</b>	<b>Mon 12/7/09</b>	<b>Mon 12/7/09</b>
22	<i>Initiating</i>	<i>N/A</i>	<i>ADM</i>	<i>Concept State Completed</i>		<i>0 days</i>	<i>Mon 12/7/09</i>	<i>Mon 12/7/09</i>
23	<b>Planning</b>	<b>N/A</b>	<b>Stage</b>	<b>Planning Stage</b>		<b>32 days</b>	<b>Tue 12/8/09</b>	<b>Fri 1/29/10</b>
24	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Project Management Plan</b>		<b>11 days</b>	<b>Tue 12/8/09</b>	<b>Thu 12/24/09</b>
25	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Scope Management Plan</b>		<b>11 days</b>	<b>Tue 12/8/09</b>	<b>Thu 12/24/09</b>
37	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Change Control Management Plan</b>		<b>9 days</b>	<b>Tue 12/8/09</b>	<b>Tue 12/22/09</b>
46	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Human Resources Plan</b>		<b>9 days</b>	<b>Tue 12/8/09</b>	<b>Tue 12/22/09</b>
55	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Communication Management Plan</b>		<b>9 days</b>	<b>Tue 12/8/09</b>	<b>Tue 12/22/09</b>
64	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Risk Management Plan</b>		<b>11 days</b>	<b>Tue 12/8/09</b>	<b>Thu 12/24/09</b>
74	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Cost Management Plan</b>		<b>11 days</b>	<b>Tue 12/8/09</b>	<b>Thu 12/24/09</b>
84	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Schedule Management Plan</b>		<b>11 days</b>	<b>Tue 12/8/09</b>	<b>Thu 12/24/09</b>
94	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Quality Management Plan</b>		<b>10 days</b>	<b>Tue 12/8/09</b>	<b>Wed 12/23/09</b>
103	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Procurement Management Plan</b>		<b>10 days</b>	<b>Tue 12/8/09</b>	<b>Wed 12/23/09</b>
112	<b>Planning</b>	<b>N/A</b>	<b>PMP</b>	<b>Contract Management Plan</b>		<b>10 days</b>	<b>Tue 12/8/09</b>	<b>Wed 12/23/09</b>
121	<i>Planning</i>	<i>N/A</i>	<i>PMP</i>	<i>Project Management Plan Complete</i>		<i>0 days</i>	<i>Thu 12/24/09</i>	<i>Thu 12/24/09</i>
122	<b>Planning</b>	<b>N/A</b>	<b>Org</b>	<b>Organizational Readiness Plan</b>		<b>13 days</b>	<b>Wed 12/23/09</b>	<b>Wed 1/13/10</b>
131	<b>Planning</b>	<b>N/A</b>	<b>M&amp;O</b>	<b>Maintenance &amp; Operation Transition Plan</b>		<b>32 days</b>	<b>Tue 12/8/09</b>	<b>Fri 1/29/10</b>
140	<b>Executing</b>	<b>N/A</b>	<b>Stage</b>	<b>Executing Stage</b>		<b>222.5 days</b>	<b>Mon 11/2/09</b>	<b>Tue 10/26/10</b>
141	<b>Executing</b>	<b>N/A</b>	<b>ADM</b>	<b>Monitoring and Controlling</b>		<b>206.5 days</b>	<b>Wed 12/2/09</b>	<b>Tue 10/26/10</b>
142	Executing	N/A	Meet	Project Status Meetings		206.1 days	Wed 12/2/09	Tue 10/26/10
195	Executing	N/A	Meet	Risk Management Meetings		201.1 days	Wed 12/2/09	Tue 10/19/10
208	Executing	N/A	RPT	Weekly Status Reports		206.5 days	Wed 12/2/09	Tue 10/26/10

Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	


ID		Stage	SDLC Phase	Deliverable	Task Name	Schedule Status	Duration	Start	Finish
257		Executing	N/A	ADM	Project Workplan Updates		85 days	Wed 12/2/09	Tue 4/27/10
310		Executing	N/A	Meet	Lessons Learned Meetings		40.1 days	Wed 12/2/09	Tue 2/9/10
313		Executing	N/A	RPT	Vendor's XX Monthly Activity Reports		190 days	Wed 12/2/09	Fri 10/1/10
326		Executing	N/A	DED	Vendor's XX Monthly Deliverables		190 days	Wed 12/2/09	Fri 10/1/10
339		Executing	N/A	ADM	Benefit Validation		52 days	Mon 11/2/09	Mon 2/1/10
342		Closing	N/A	PIER	Closing Stage		5 days	Thu 10/29/09	Wed 11/4/09

Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

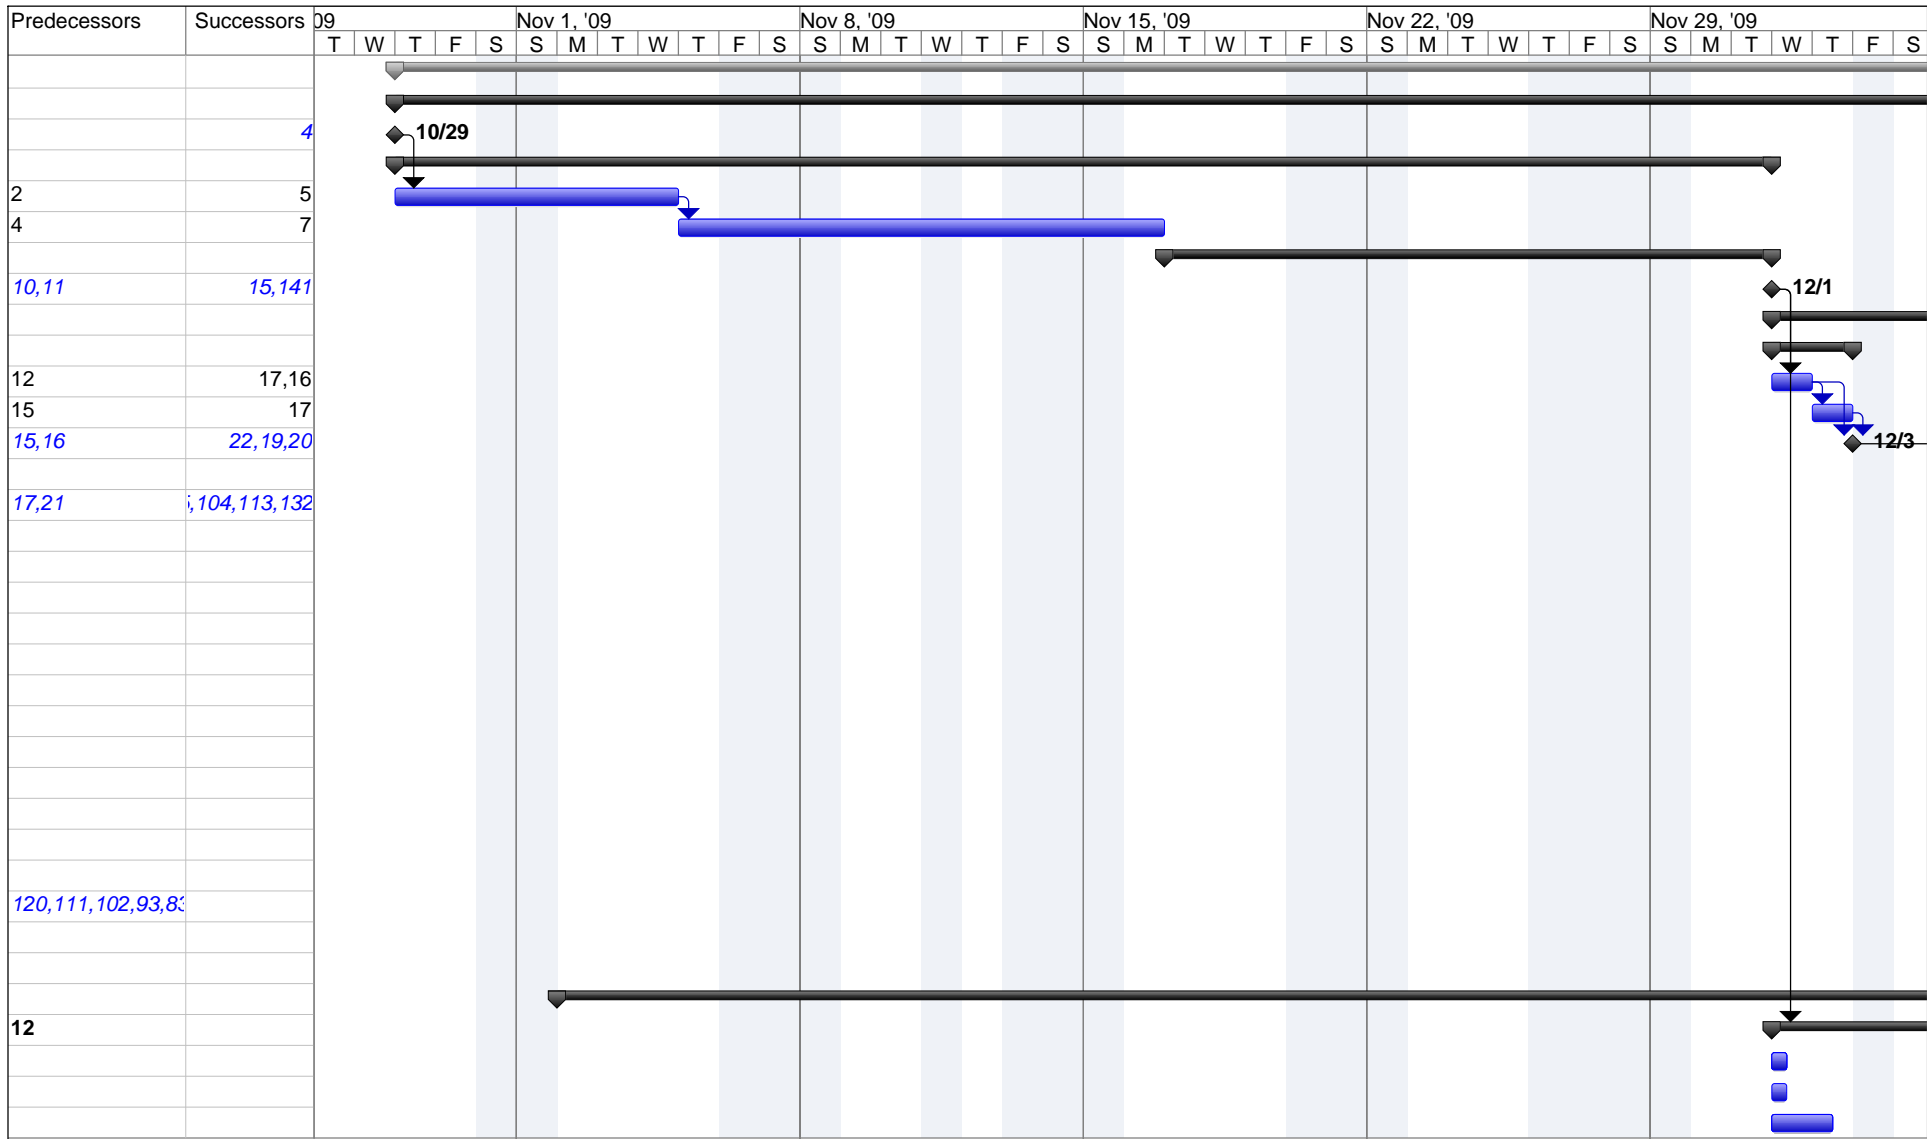


Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	



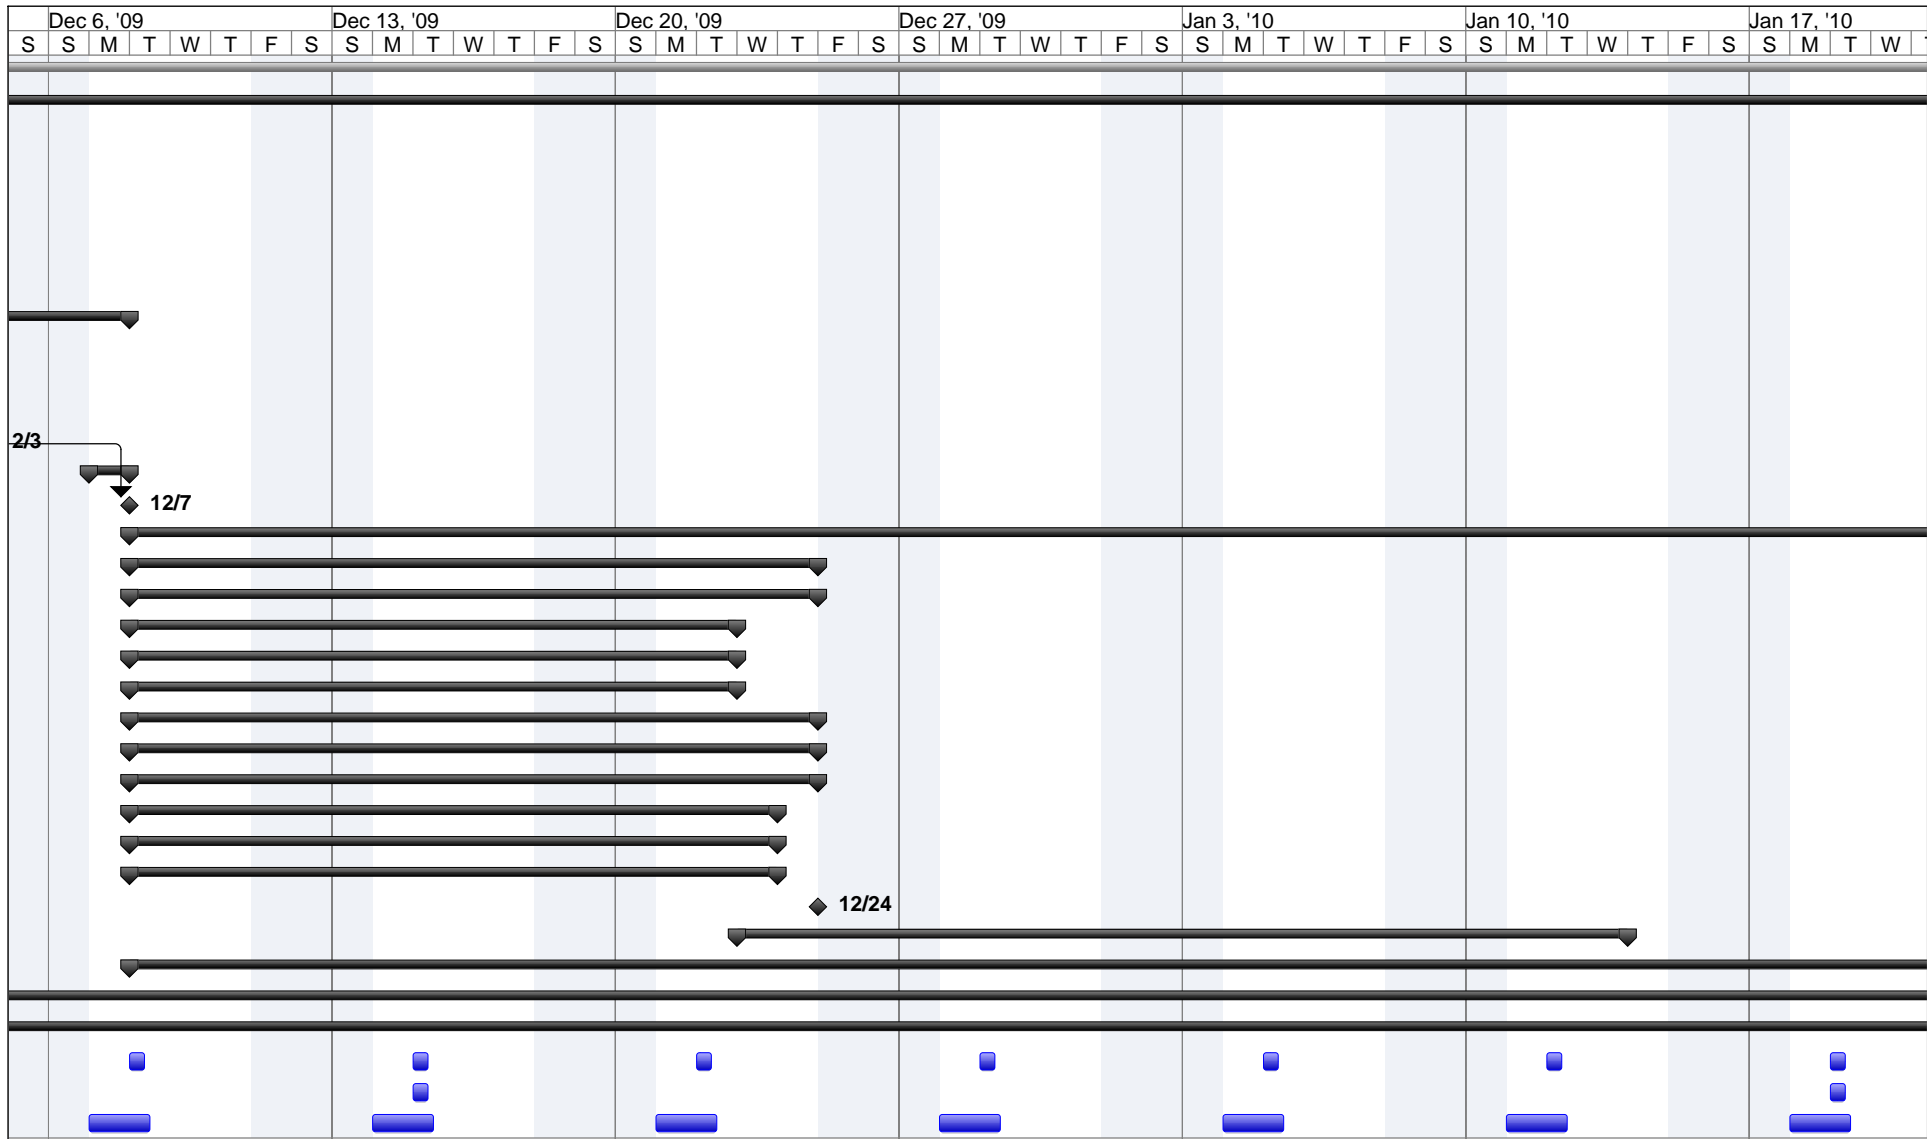


Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	



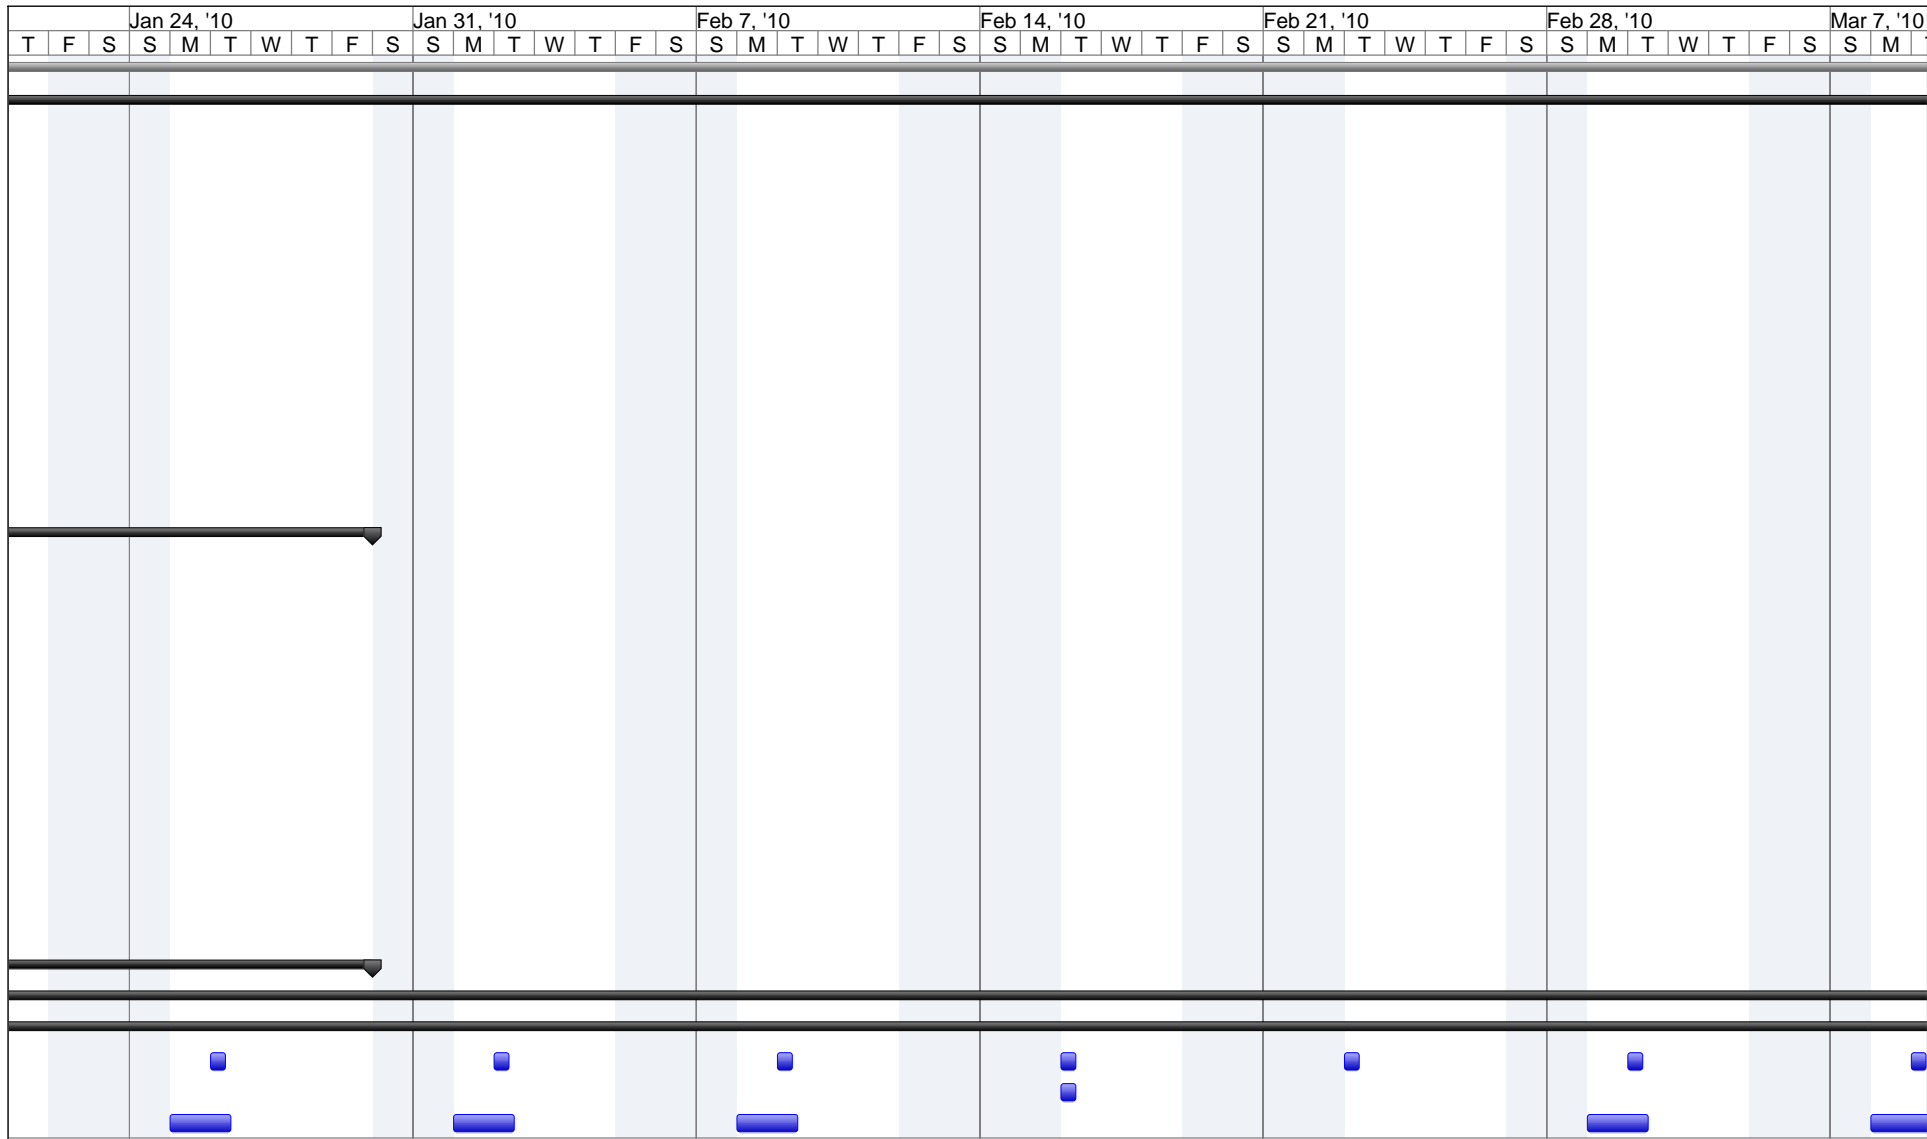


Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	




Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	




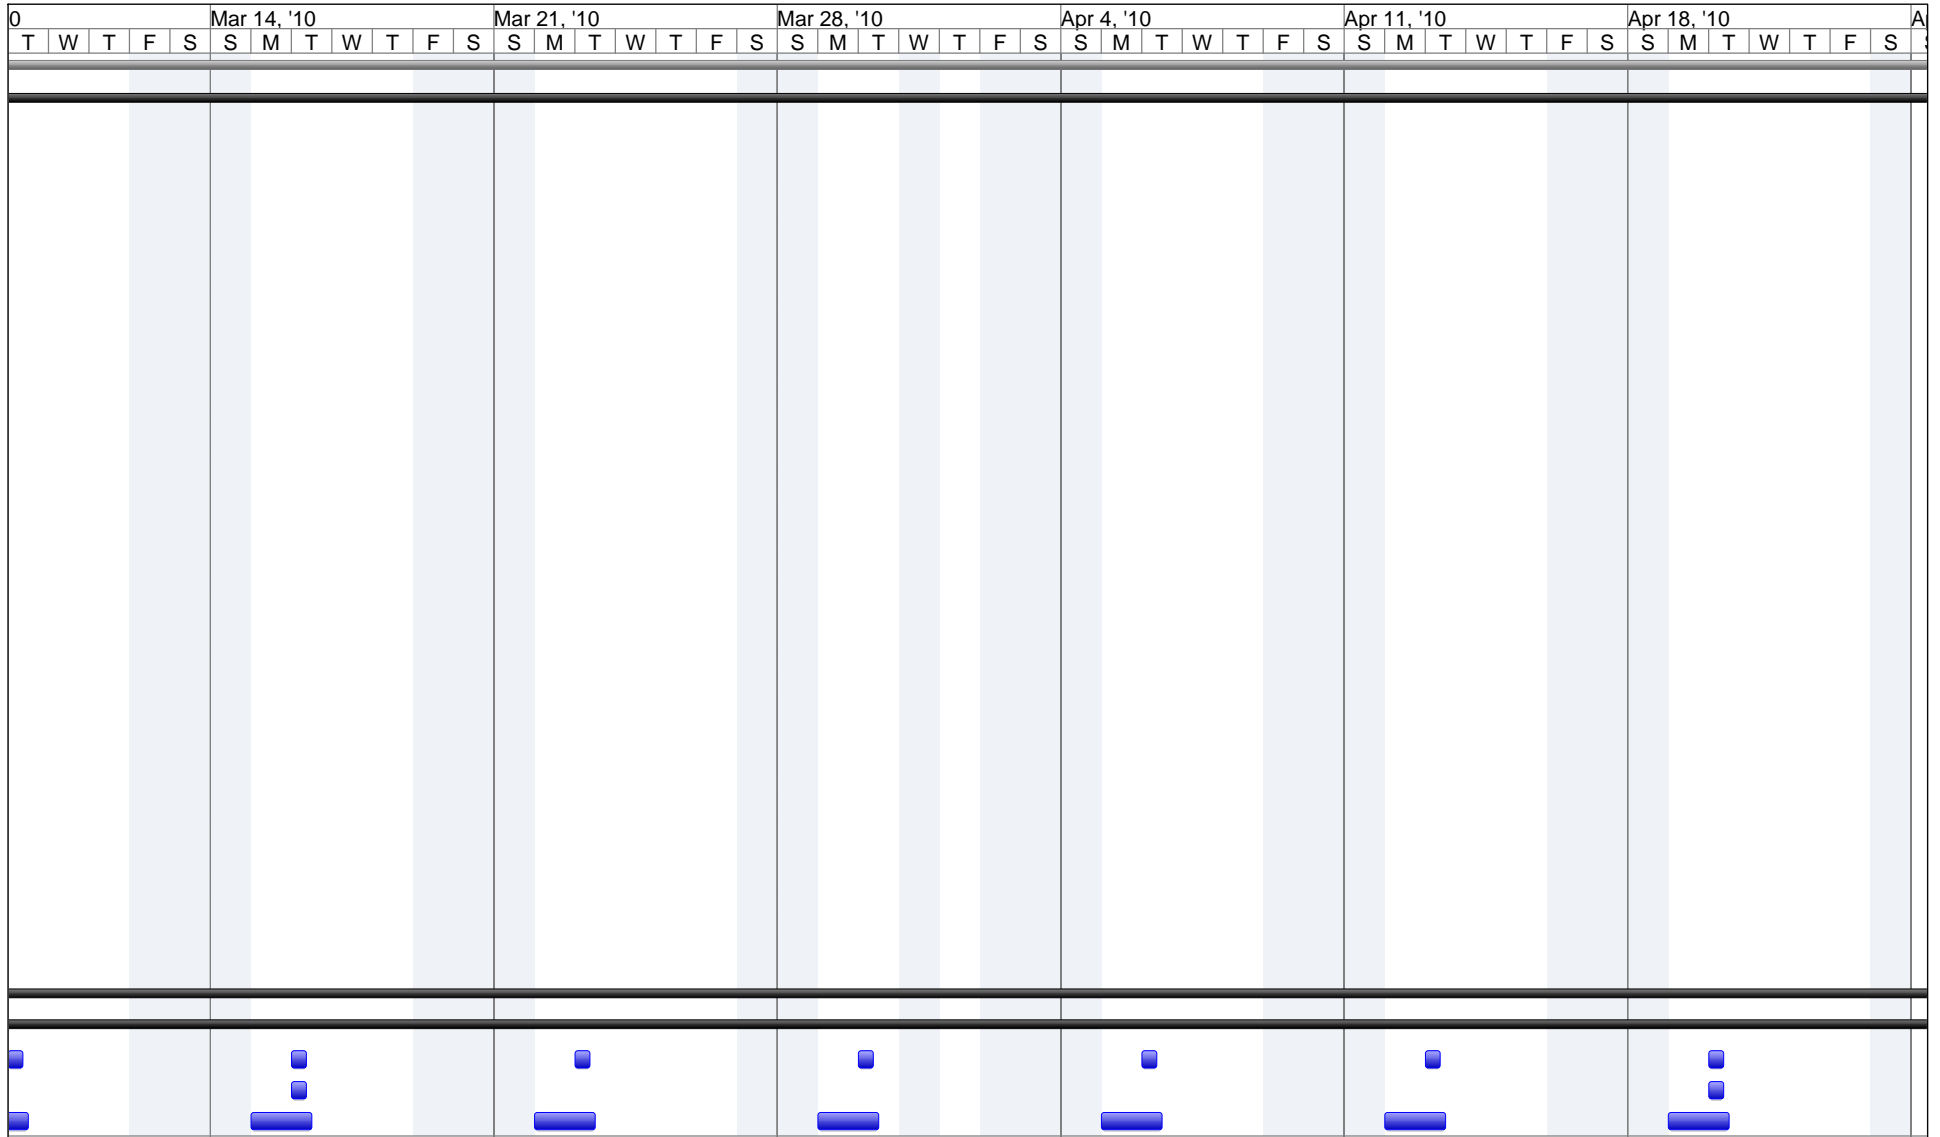


Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	




Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

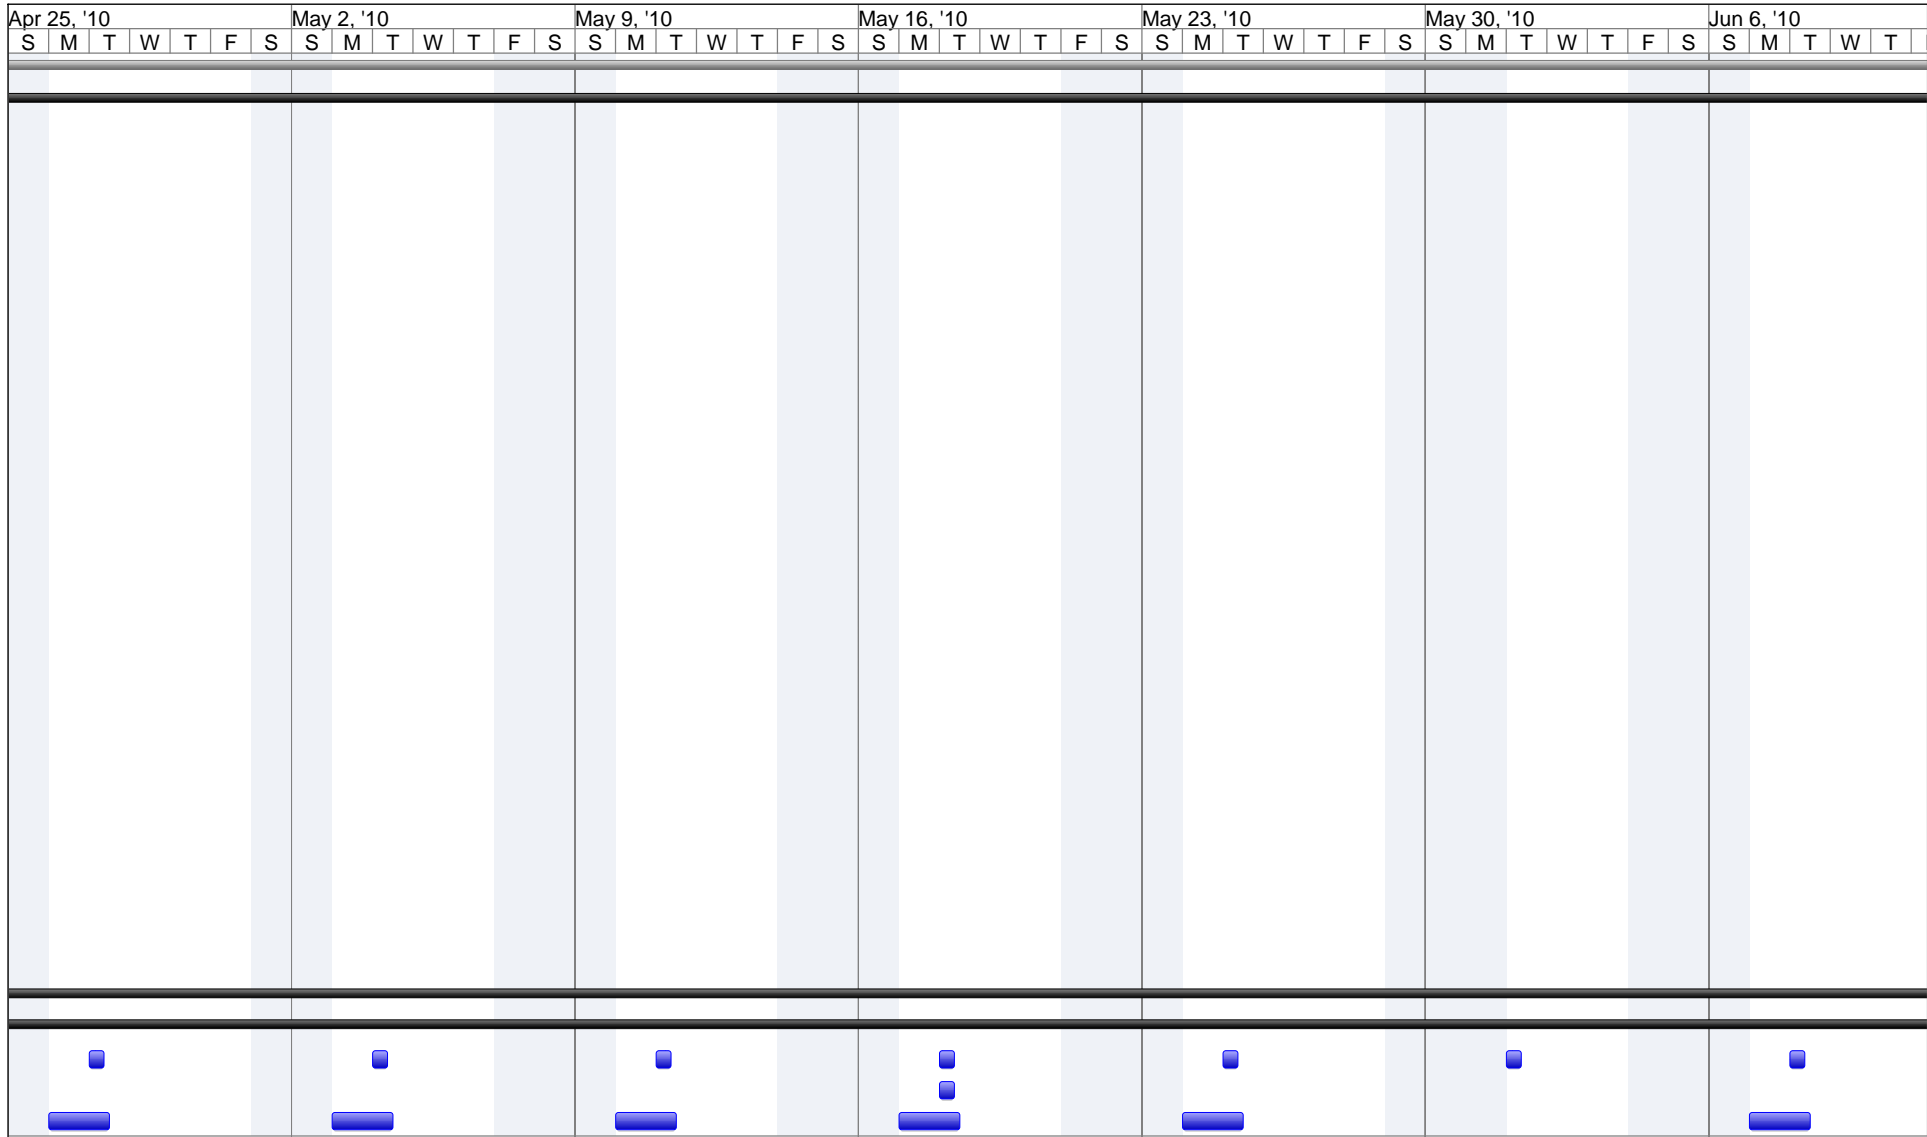

Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	





Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

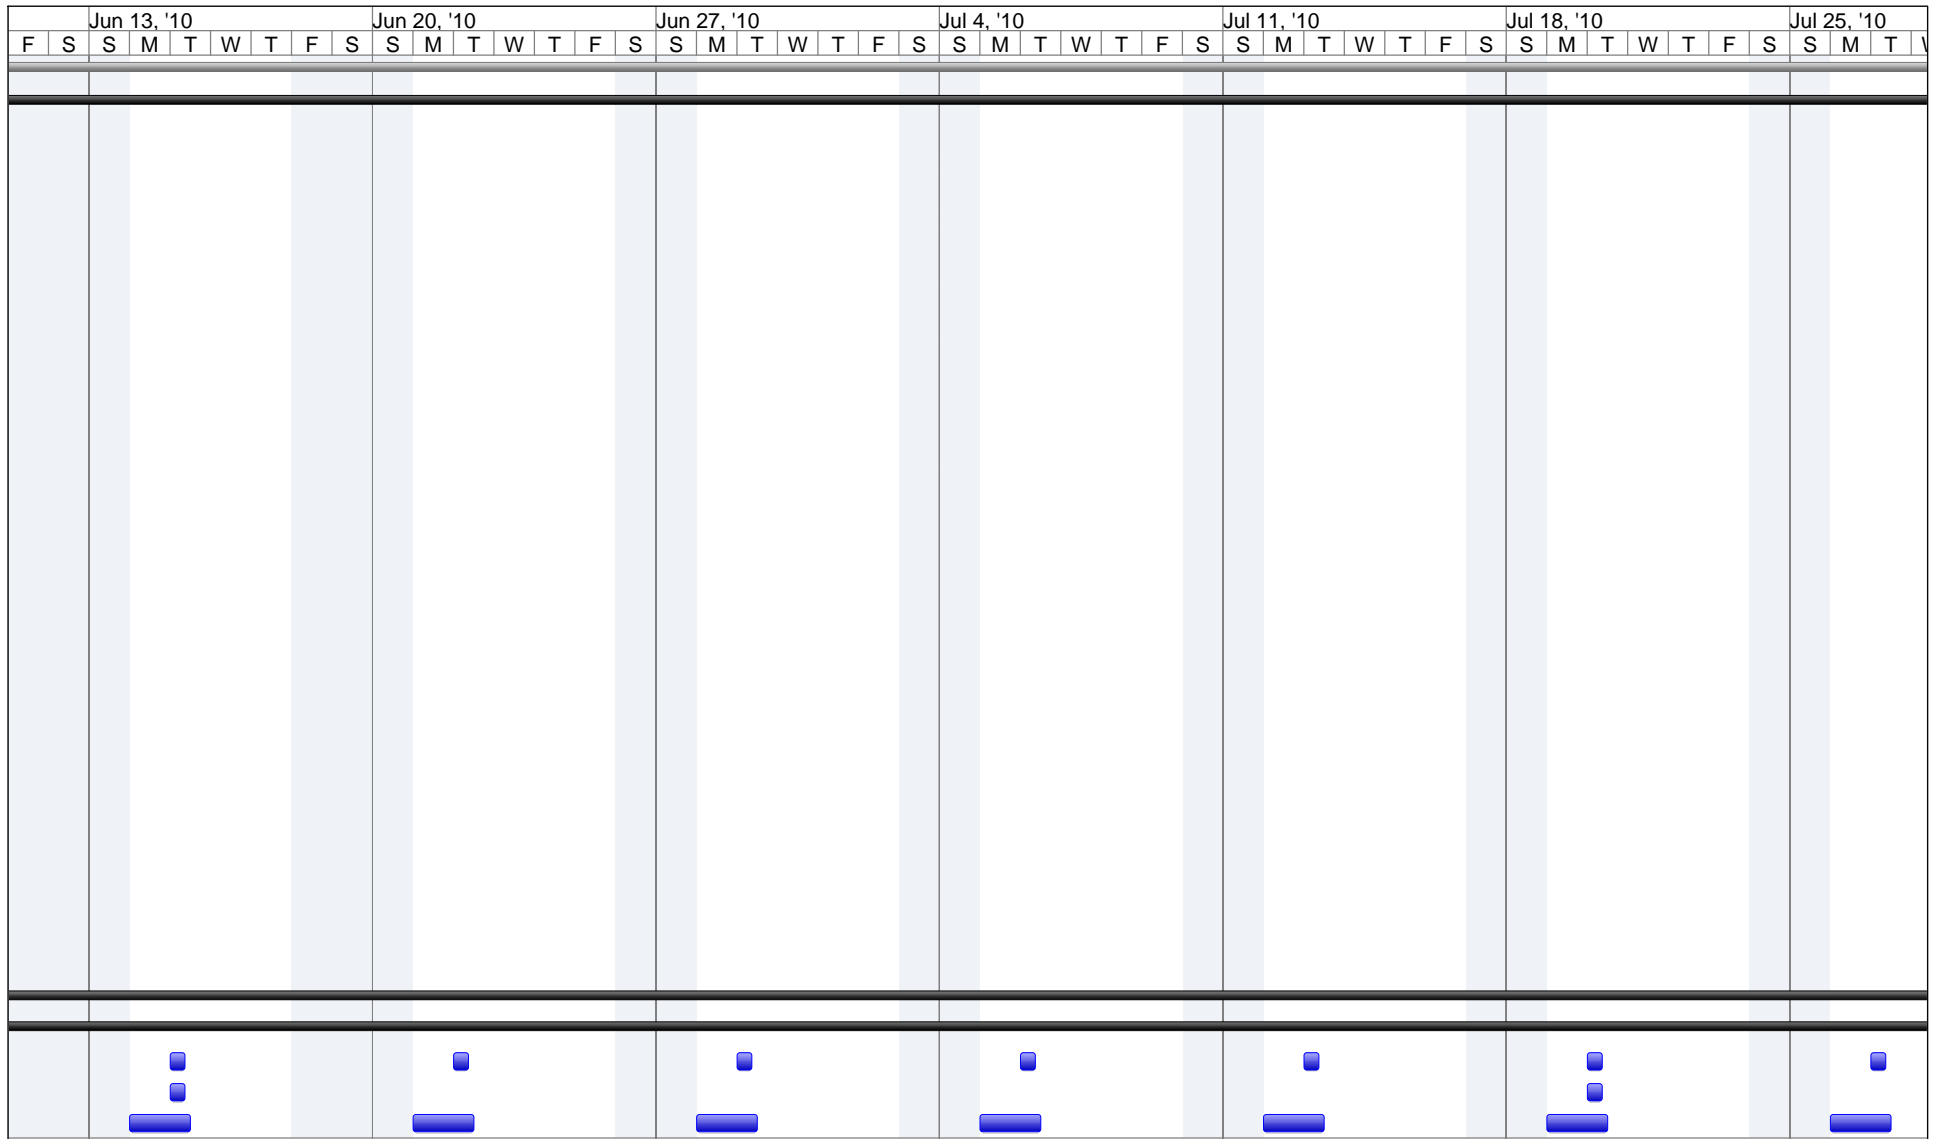


Project: Project Work Plan (Schedule)  
Date: Thu 5/19/11



Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	



Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

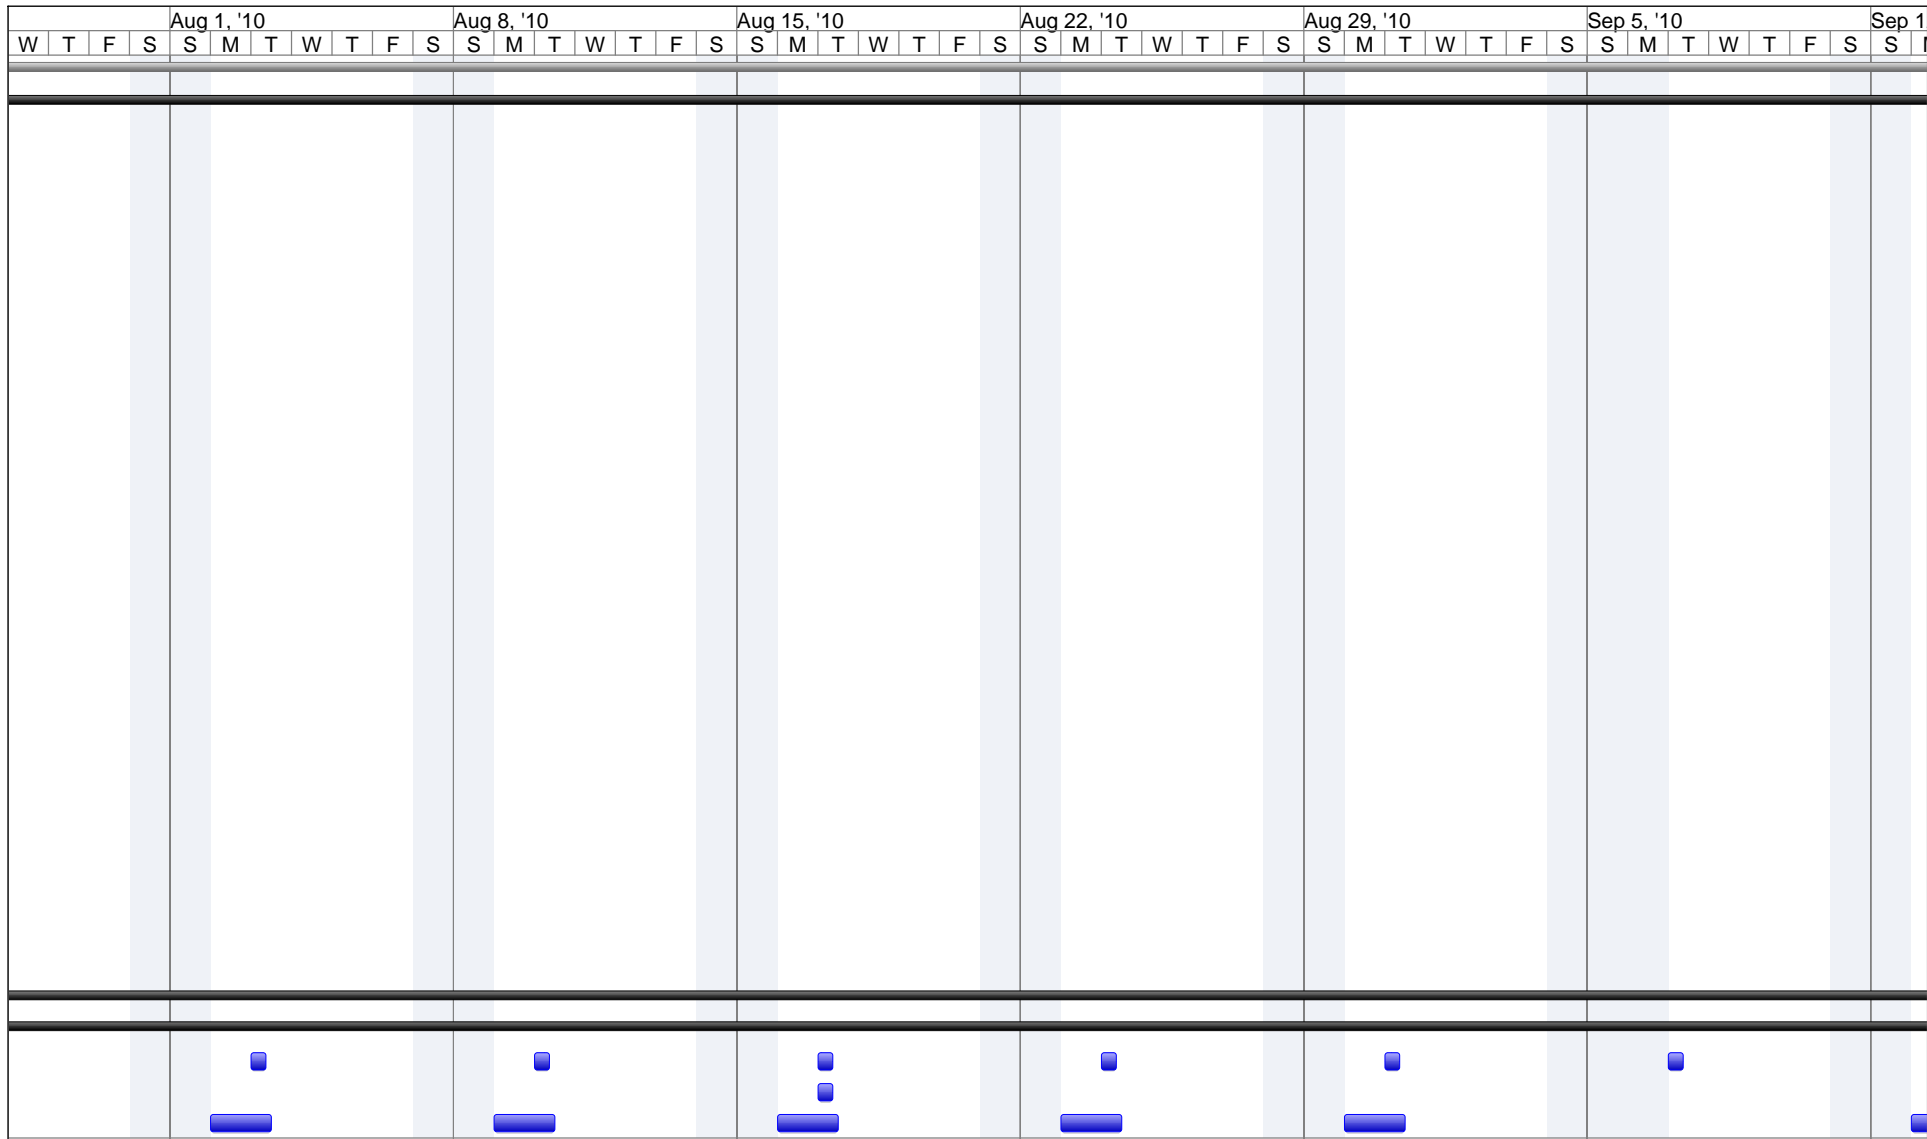


Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	




Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	



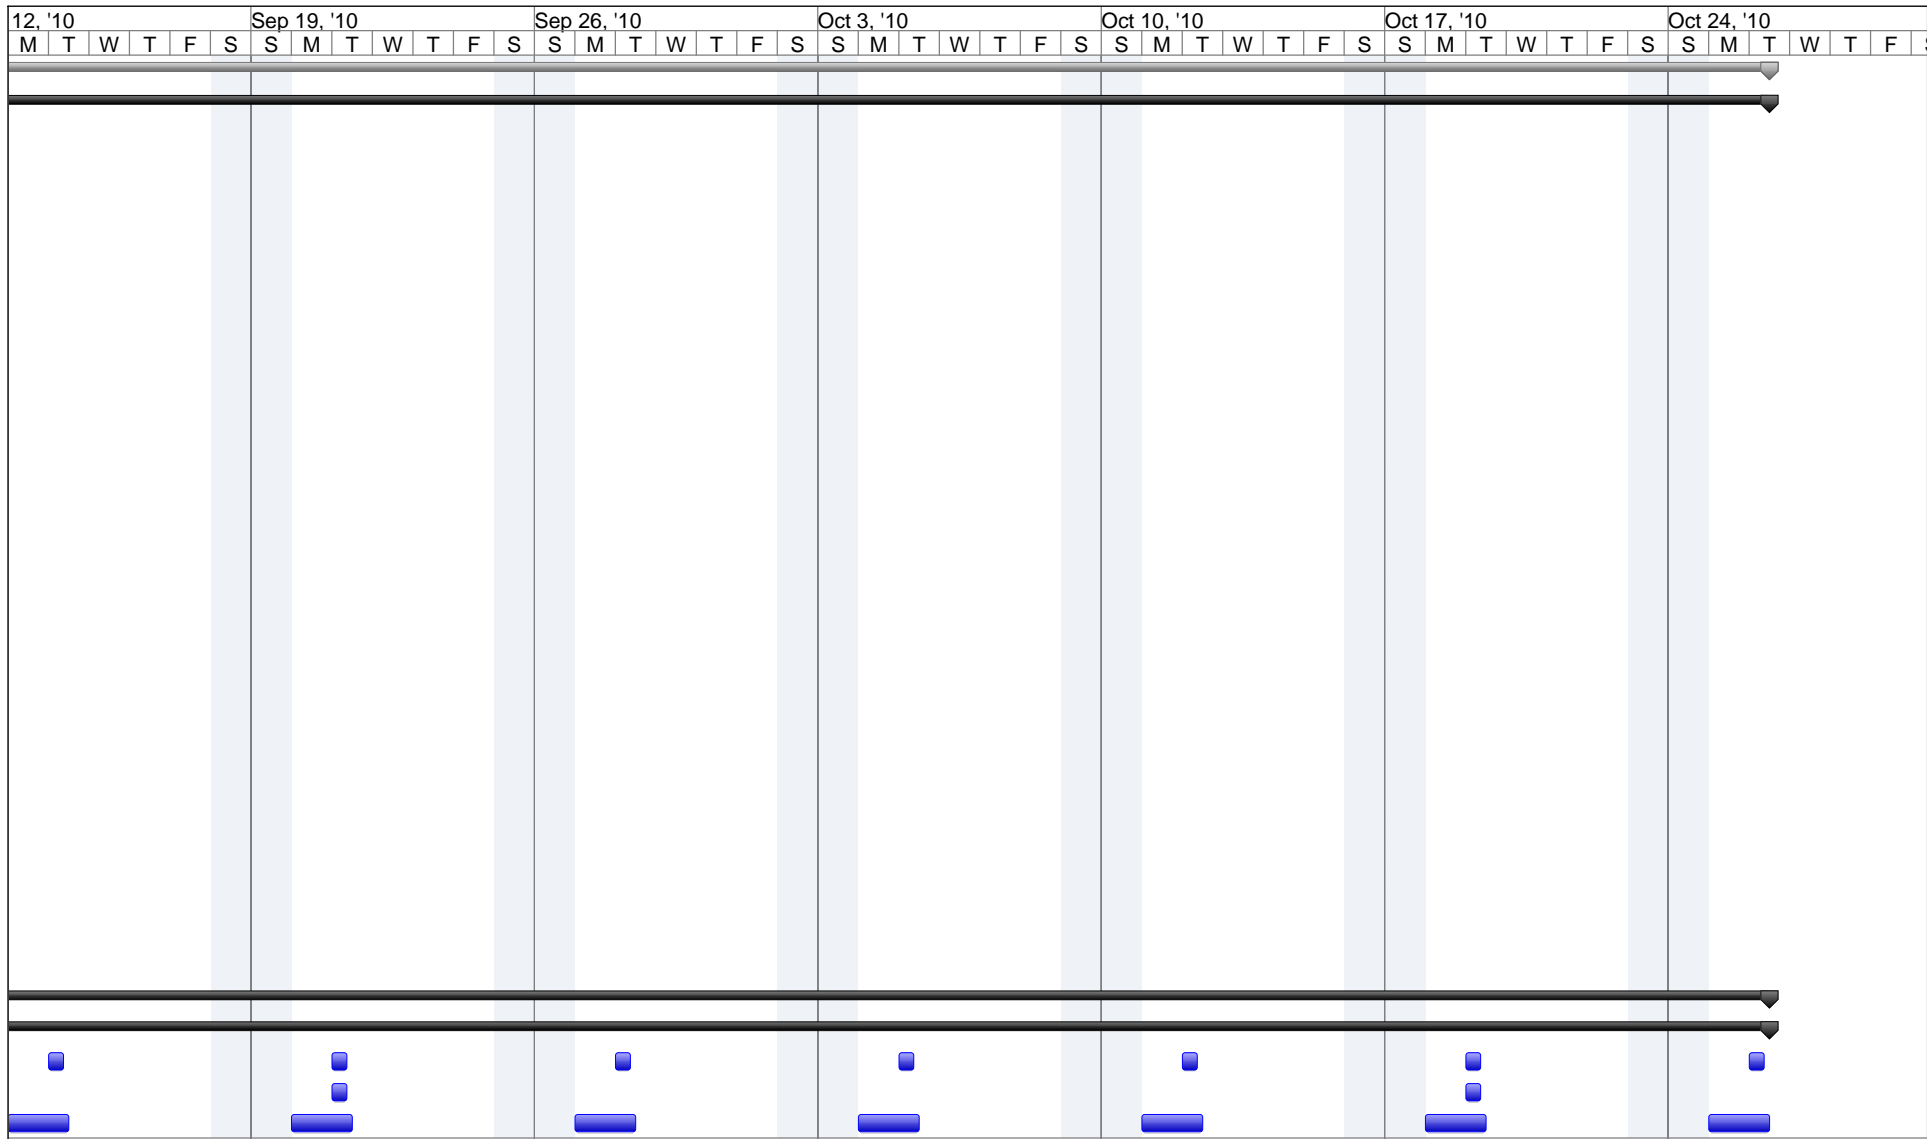

Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	



Project: Project Work Plan (Schedule) Date: Thu 5/19/11	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	
